

LEARNING RESOURCES CENTER MERCED COLLEGE



Merced Community College
Monthly Project Report
Learning Resources



Project Team

Architect/Engineer

Lionakis Beaumont Design Group
Dave Younger— Principal
Jonathan McMurtry— Proj Mgr
Turley and Associates
Ken Rubitsky & Associates
Smith, Fause & McDonald, Inc.
David Bigler Associates

Construction Manager

Parsons Brinckerhoff Constr Svcs
Bruce Rich— Project Executive
Alex Belanger— Project Mgr
Ken Schultz— Proj Super
Aida Ramos - Project Admin

Inspector Of Record

United Inspection Services
John Hill

Facility Delivery Team

Terry Ruscoe— Director Facilities
Rick Souhrada— Director Maint.
Sheila Flores— Facility Planner

COLLEGE OFFICIALS

Board of Trustees

Eugene J. Vierra-President
Robert Haden-Vice President
Jinet Troost-Clerk
Les McCabe-Member
Eva de Long-Member
Lewis Braxton-Member
Jim Glidden-Member

Executive Administration

Benjamin Duran— President
Larry Johnson—VP Admin
John Spevak—VP Instruction
Ann Newins— VP Student Svcs
Mike Cuchna—Assoc. VP
Harry Gossett— Dean
Sarah Greene— Dean
Robert Lenz— Dean
Karyn Wiens— Dean
Jim Bonstein—Dean

Project Overview

The new Learning Resources Center will provide expanded learning opportunities for the students and staff of Merced College and the Merced Community. The 67,000 square foot facility will have a state of the art data network system that will allow visitors access to a wide range of electronic media as well as the resources of the World Wide Web through a high capacity Internet connection. The facility will provide numerous study areas as well as meeting rooms and group study rooms. The book stack area will provide space for 50,000 volumes. The facility is scheduled for occupancy in Spring 2007.




PROJECT STATUS REPORT

Original Contracts	\$	13,720,213
Approved Changes	\$	(18,522)
Pending Changes	\$	108,179
Current Contracts	\$	13,809,870
% Changes		0.653%

Monthly Report Number 11
August 2006

Work Scheduled for the next Six Weeks

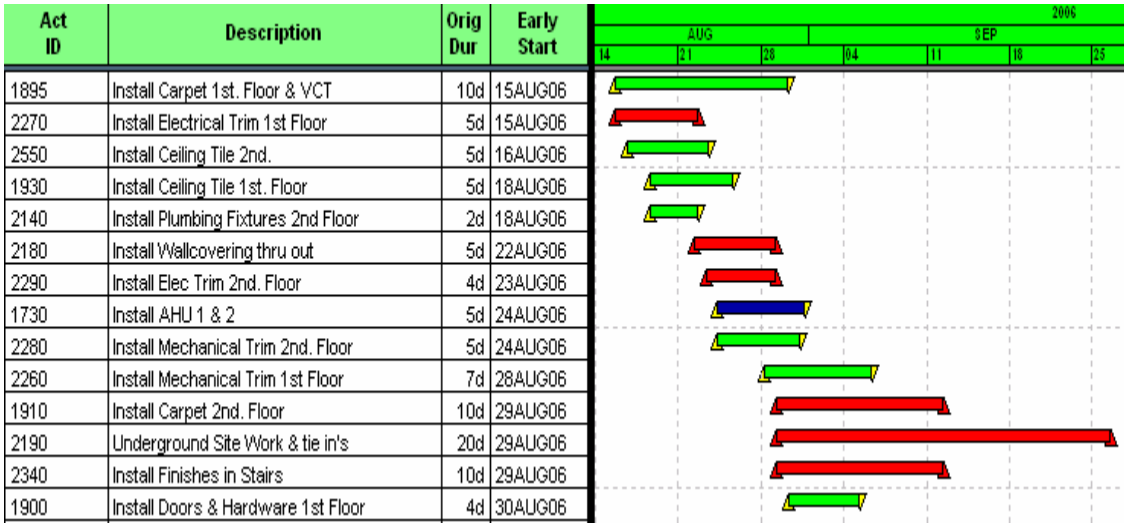

Interior Finishes



- This Month Activities**
- Complete Drywall Taping
 - Complete Windows
 - Complete Metal Panels
 - Continue Plumbing
 - Begin Site Work

- Next Month Planned Activities**
- Site concrete
 - Glass installation
 - Millwork installation
 - Extension of chilled and hot water lines for future
 - Fabric wall covering
 - Light fixture installation
 - Starting sprinkler system



Progress on schedule

