

# LEARNING RESOURCES CENTER MERCED COLLEGE



Merced Community College  
Monthly Project Report  
Learning Resources



## Project Team

### Architect/Engineer

*Lionakis Beaumont Design Group*  
Dave Younger— Principal  
Jonathan McMurtry— Proj Mgr  
Turley and Associates  
Ken Rubitsky & Associates  
Smith, Fause & McDonald, Inc.  
David Bigler Associates

### Construction Manager

*Parsons Brinckerhoff Constr Svcs*  
Bruce Rich— Project Executive  
Alex Belanger— Project Mgr  
Ken Schultz— Proj Super  
Aida Ramos - Project Admin

### Inspector Of Record

*United Inspection Services*  
John Hill

### Facility Delivery Team

Terry Ruscoe— Director Facilities  
Rick Souhrada— Director Maint.  
Sheila Flores— Facility Planner

## COLLEGE OFFICIALS

### Board of Trustees

Eugene J. Vierra-President  
Robert Haden-Vice President  
Jinet Troost-Clerk  
Les McCabe-Member  
Eva de Long-Member  
Lewis Braxton-Member  
Jim Glidden-Member

### Executive Administration

Benjamin Duran— President  
Larry Johnson—VP Admin  
John Spevak—VP Instruction  
Ann Newins— VP Student Svcs  
Mike Cuchna—Assoc. VP  
Harry Gossett— Dean  
Sarah Greene— Dean  
Robert Lenz— Dean  
Karyn Wiens— Dean  
Jim Bonstein—Dean

## Project Overview

The new Learning Resources Center will provide expanded learning opportunities for the students and staff of Merced College and the Merced Community. The 67,000 square foot facility will have a state of the art data network system that will allow visitors access to a wide range of electronic media as well as the resources of the World Wide Web through a high capacity Internet connection. The facility will provide numerous study areas as well as meeting rooms and group study rooms. The book stack area will provide space for 50,000 volumes. The facility is scheduled for occupancy in Spring 2007.




## PROJECT STATUS REPORT

Original Contracts	\$	13,721,149
Approved Changes	\$	14,722
Pending Changes	\$	138,429
Current Contracts	\$	13,874,300
% Changes		1.116%

Monthly Report Number 12  
September 2006

## Work Scheduled for the next Six Weeks

## Interior Finishes

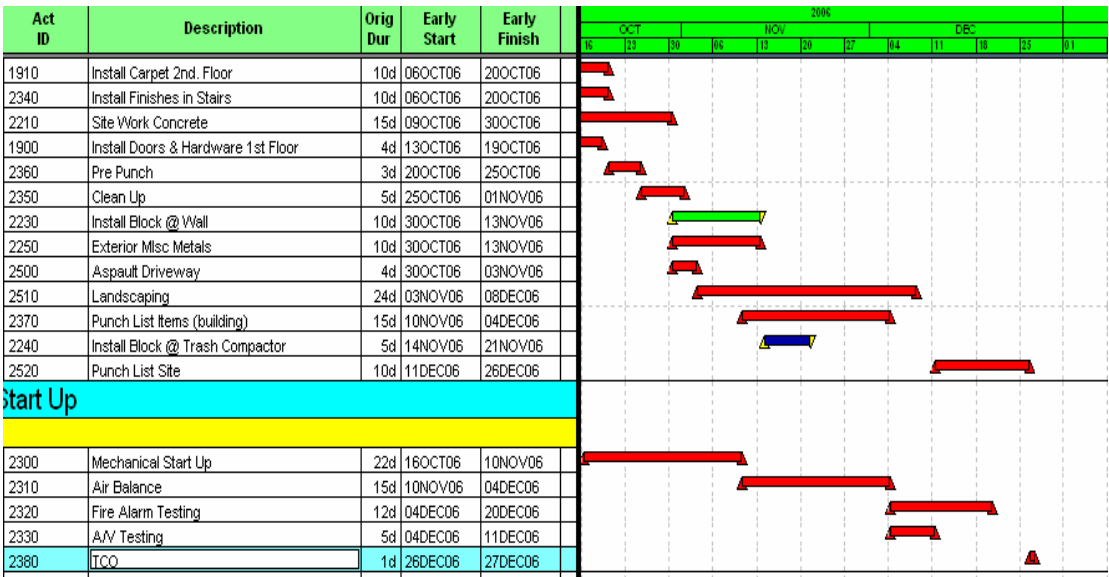

## Progress on schedule

- This Month Activities**
- Site concrete
  - Glass installation
  - Millwork installation
  - Extension of chilled and hot water lines for future
  - Fabric wall covering
  - Light fixture installation
  - Starting sprinkler system

- Next Month Planned Activities**
- Pouring sidewalks around the building
  - Pouring the stair pans throughout the building
  - Landscaping starting
  - Block work in front of the building (seats)
  - Starting to install ceiling tile
  - Glass to be installed second floor
  - Cabinets on going
  - Wainscot to start 1st floor
  - Computer floor to start

