

# ALLIED HEALTH CENTER-PHASE 2 MERCED COLLEGE



Merced Community College  
Monthly Project Report  
Allied Health Center—Phase 2



## PROJECT TEAM

### Architect/Engineer

*Lionakis Beaumont Design Group*  
Dave Younger, Principal  
Toby Insinna, Project Manager  
Turley and Associates  
Ken Rubitsky & Associates  
Smith, Fause & McDonald, Inc.  
David Bigler Associates

### Construction Manager

*PB Americas, Inc*  
Bruce Rich, Project Executive  
Tony Valdez, Project Manager  
Sara Alvarado, Project Engineer

### Inspector Of Record

*United Inspection Services,*  
Carl Horner  
Jim Womack

### Facility Delivery Team

Joe Bisinger, Purchasing/Facilities  
Lead  
Rick Souhrada, Facilities  
Construction Director  
Sheila Flores, Facilities Planner

## COLLEGE OFFICIALS

### Board of Trustees

Jinet Troost, President  
Lewis S. Braxton, Vice-President  
Eva de Long, Clerk  
Jim Glidden, Member  
Les McCabe, Member  
Eugene J. Vierra, Member  
Robert Haden, Member

### Executive Administration

Benjamin Duran, President  
Larry Johnson, VP Admin  
John Spevak, VP Instruction  
Anne Newins, VP Student Svcs  
Mike Cuchna, Assoc. VP  
Sarah Greene, Dean  
Karyn Wiens, Dean  
Bobby Anderson, Dean  
Bob Taylor, Dean  
Betsy Donovan, Interim Dean

## Project Overview

The Allied Health Center will provide expanded learning opportunities for the students and staff of Merced College and the Merced Community. The project consists of 2 buildings totaling 28,000 SF. The buildings include x-ray suites, offices, meeting rooms, study rooms and classrooms. The Project is scheduled to be completed Spring of 2009.



## PROJECT STATUS REPORT

Original Contracts	\$7,049,319.00
Approved Changes	\$0.00
Pending Changes	\$0.00
Current Contracts	\$7,049,319.00
% Changes	0.000%

Monthly Report Number 2  
February 2008

# Work Schedule

ID		Task Name	Duration
1		Notice to proceed	1 day
2		MOBILIZATION	4 days
3		SITE SURVEY AND STAKING	2 days
44		UNDERGROUND WET UTILITIES	20 days
46		UNDERGROUND ELECTRICAL	12 days
4		EAST BLDG FOOTINGS & FORMS	7 days
5		EASY BLDG CONCRETE SLAB	6 days




This Month Activities (February 2008)

- Reinforcement for footings

Next Month Activities (March 2008)

- Working on the slab for the East Building

## Progress on Schedule

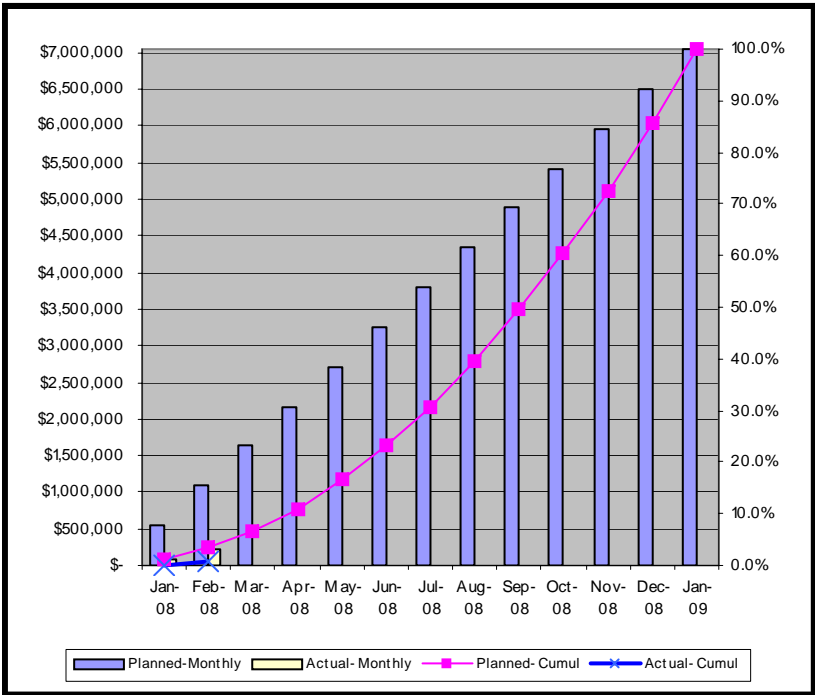

Forms at the East Building Footings
